# Preliminary

# Site Mass Demolition

PBCDF

PBCDF INAS DAILY SCHEDULE- Working

| Activity ID | Activity Name | Projected or Actual (A) Start | Projected or Actual (A) Finish | Cal ID | Rem Dur |
|---|---|---|---|---|---|
| **MDB Demolition** | | | | | |
| **Subcontract Development** | | | | | |
| CLMDBDO95 | Closure - SCM Develop Demolition SOW RFP | 01-Aug-11 08:00 A | 05-Aug-11 17:00 | 5 | 16h |
| CLMDBDO100 | Closure - Demolition SOW RFP Bid Period | 08-Aug-11 08:00 | 27-Oct-11 17:00 | 5 | 464h |
| CLMDBDO105 | Closure - Demolition RFP Pre-Bid Meeting | 12-Sep-11 08:00* | 13-Sep-11 17:00 | 5 | 16h |
| CLMDBDO110 | Closure - Demolition Contractor Bid Review | 28-Oct-11 08:00 | 01-Dec-11 17:00 | 5 | 184h |
| CLMDBDO115 | Closure - Demolition Subcontract Award Period | 02-Dec-11 08:00 | 15-Dec-11 17:00 | 5 | 80h |
| CLMDBDO120 | Demolition Subcontract Awarded | | 15-Dec-11 17:00 | 5 | 0h |
| **SITE Demo Sub Management Plan** | | | | | |
| CLSITESUB-100 | Site Sub - Draft Management Plan | 16-Dec-11 07:00 | 14-Jan-12 17:00 | 7 | 300h |
| CLSITESUB-110 | Site Sub - URS Review & Comment on Draft Management Plan | 15-Jan-12 07:00 | 13-Feb-12 17:00 | 7 | 300h |
| CLSITESUB-120 | Site Sub - Finalize Management Plan | 14-Feb-12 07:00 | 14-Mar-12 17:00 | 7 | 300h |
| CLSITESUB-160 | Site Sub - Draft Milestones & Schedule | 15-Mar-12 07:00 | 13-May-12 17:00 | 7 | 600h |
| CLSITESUB-170 | Site Sub - URS Review & Comment on Draft Milestones & Schedule | 14-May-12 07:00 | 12-Jun-12 17:00 | 7 | 300h |
| CLSITESUB-180 | Site Sub - Finalize Milestones & Schedule | 13-Jun-12 07:00 | 12-Jul-12 17:00 | 7 | 300h |
| CLSITESUB-190 | Site Sub - Mobilize to Site | 26-Jul-12 07:00 | 24-Aug-12 17:00 | 7 | 300h |
| CLSITESUB-200 | Site Subcontractor Perform Mass Demo of Site | 25-Aug-12 07:00 | 20-Feb-13 17:00 | 7 | 1800h |
| **Demo Sub Health & Safety Plan (HASP)** | | | | | |
| CLSITESUB-130 | Site Sub - Draft Health & Safety Plan (HASP) | 27-Apr-12 07:00 | 25-Jun-12 17:00 | 7 | 600h |
| CLSITESUB-140 | Site Sub - URS Review & Comment on Draft Health & Safety Plan (HASP) | 26-Jun-12 07:00 | 10-Jul-12 17:00 | 7 | 150h |
| CLSITESUB-150 | Site Sub - Finalize Health & Safety Plan (HASP) | 11-Jul-12 07:00 | 25-Jul-12 17:00 | 7 | 150h |

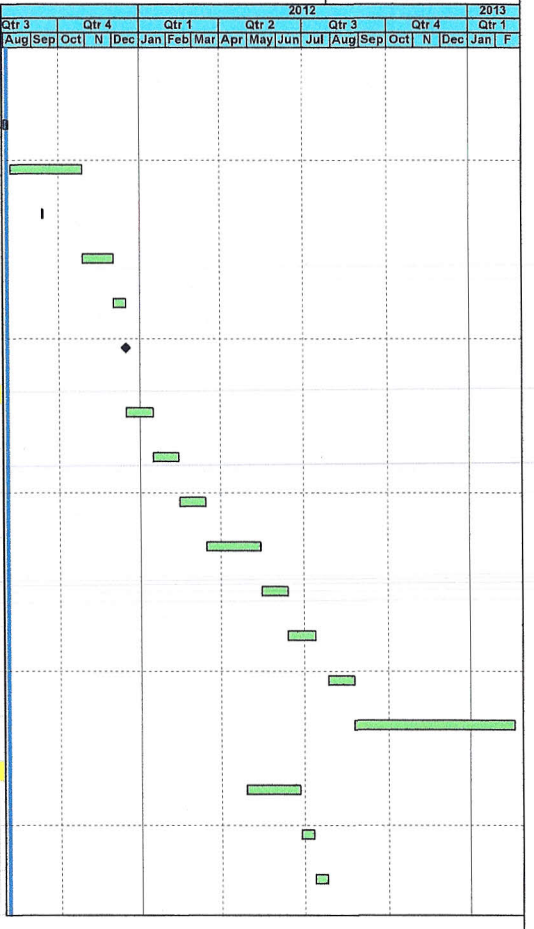


Section J, Attachment 25
